March 2013

Quarterly Report

IEN Program Resource Advisory Council

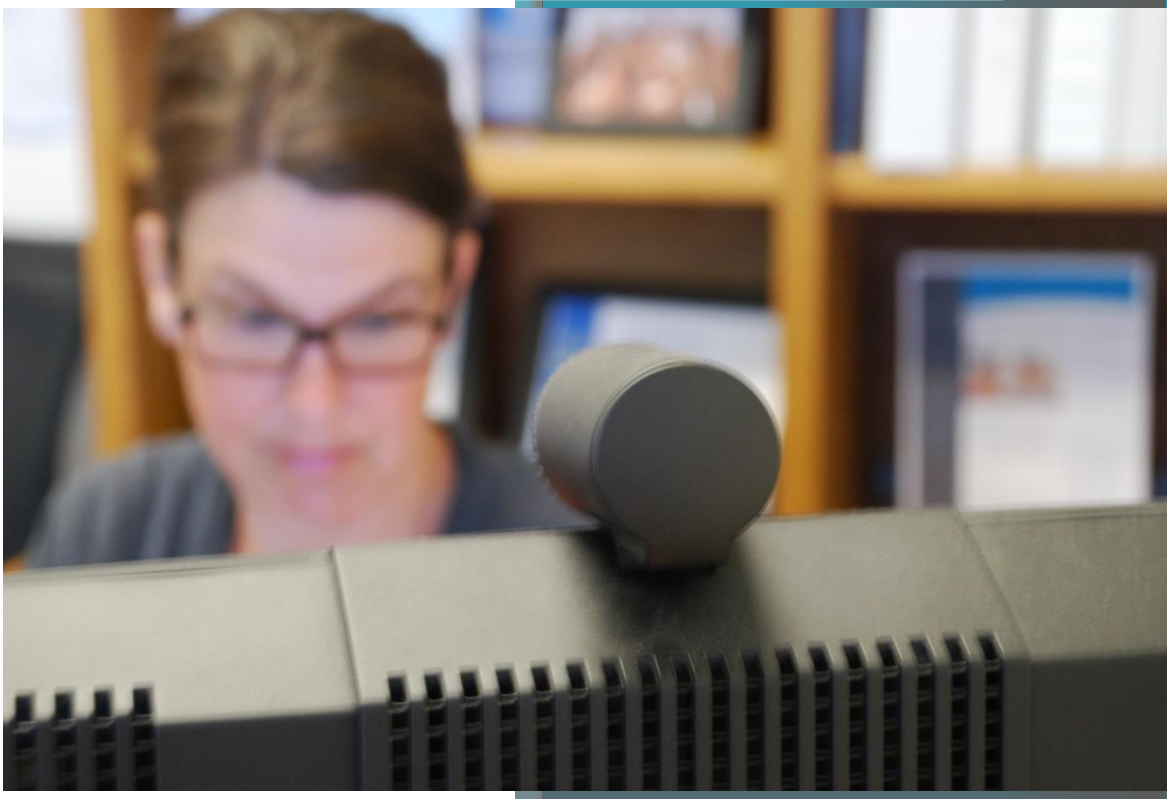

Idaho Education Network

This page intentionally left blank

COUNCIL MEMBERS

SUPERINTENDENT OF PUBLIC INSTRUCTION

Supt. Tom Luna (Chairman)

CEO, IDAHO DIGITAL LEARNING ACADEMY

Dr. Cheryl Charlton

DIRECTOR, DEPT. OF ADMINISTRATION

Teresa Luna (Vice Chairman)

PUBLIC AND HIGHER EDUCATION

Dr. Jerry Reininger Director, Information Systems
Meridian School District

Dr. John Miller Dean, Off Campus Instruction
College of Southern Idaho

PRIVATE SECTOR

Shelly Sayer VP of Finance
Premier Technology, Inc

Jay Larsen Executive Director
Idaho Technology Council

CHAIRMAN, HOUSE OF REPRESENTATIVES EDUCATION COMMITTEE

Representative Reed DeMordaunt

CHAIRMAN, SENATE EDUCATION COMMITTEE

Senator John Goedde

MEMBERS OF THE JOINT FINANCE AND APPROPRIATIONS COMMITTEE (JFAC)

Representative Darrell Bolz

(Vacant)

Senator Shawn Keough

(Vacant)

GOALS

The 2009 goal of the IEN in Phase One was to connect sufficient high-speed broadband capabilities to every high school in Idaho over the course of the following three years. In Phases Two and Three, the IEN will work to connect middle schools, elementary schools and libraries to sufficient high-speed broadband capabilities as well. Concurrently, a statewide network was created connecting those schools and communities to education opportunities from around the state, nation and world.

VISION

The IEN is the statewide managed network solution connecting all public education institutions. It delivers equal educational opportunities for students and communities.

MISSION

The IEN connects Idaho schools and communities to create new opportunities for the empowerment and achievement of all Idaho citizens.

BUDGETED AND ACTUAL EXPENDITURES

Idaho Education Network

FY2013 YTD Financial Summary

Updated: 6/3/2013

Fund Summaries

Fund Source	General Funds - Index 9901			J.A. and Kathryn Albertson Foundation - Index 9993				Title IID Funds - 9994				RUS Funds - 9996			
Personnel Funds															
	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Projected for Q4	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Obligated for Q4	FY2013 Funds Projected for Q4	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Obligated for Q4	FY2013 Funds Projected for Q4	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Obligated for Q4	FY2013 Funds Projected for Q4
	$ 413,600	$ 353,321	$ 60,279	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Operational Funds															
	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Projected for Q4	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Obligated for Q4	FY2013 Funds Projected for Q4	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Obligated for Q4 (Estimate)	FY2013 Funds Projected for Q4	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Obligated for Q4 (Estimate)	FY2013 Funds Projected for Q4
	$ 1,526,900	$ 1,526,900	$ 0.00	$ 485,675	$ 121,784	$ 297,654	$ 66,237	$ 184,507	$ 135,552	$ 48,955	$ -	$ 605,418	$ 549,849	$ 55,569	$ -
Capital Funds															
	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Projected for Q4	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Obligated for Q4	FY2013 Funds Projected for Q4	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Obligated for Q4	FY2013 Funds Projected for Q4	FY2013 Budget	FY2013 YTD Expenditures Spent Though 05/28/13	FY2013 Funds Obligated for Q4	FY2013 Funds Projected for Q4
	N/A	N/A	N/A	$ 100,000	$ 14,422	$ 84,514	$ 1,064	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
FY2013 E-Rate Reimbursement															
	FY2013 Budget	FY2013 YTD Based on Expenditures Though 05/28/13	FY2013 Funds Projected for Q4												
	$ 6,260,526	$ 4,039,187	$ 2,221,339												

CONNECTIVITY REPORT

	School Data						Network Data						
	District	Dist No.	City	Reg	Num HS	HS Students Served	Architecture Capacity	Current IEN Purchased BW Per District (Mbs)	BW P & L Status	Current IEN Connection Media to District Aggregation Point	Current IEN Connectivity Circuit Type	Current IEN Connection Local Loop Provider	Comments
1	ABERDEEN SD	58	ABERDEEN	5	1	239	1000.00	20.00	A Complete	Fiber	Syringa Ethernet (Agg)	Syringa	Upgrade to 20 Mbps L2 Ord 5/16/13
2	AMERICAN FALLS JOINT SD	381	AMERICAN FALLS	5	2	488	1000.00	50.00	A Complete	Fiber	Metro Ethemet (Agg)	CenturyLink	MOEUg -> 50 Mbps Acc Ord 3/19/13
3	ANOTHER CHOICE VIRTUAL CHARTER	476	NAMPA	3	1	110	1000.00	10.00	A Complete	Fiber	Metro Ethemet (Agg)	CenturyLink	
4	BASIN SD	72	IDAHO CITY	3	1	160	155.00	18.00	A Complete	Copper	12xT1-TDM (Agg)	CenturyLink	BW Inc from 10.5 -> 12 Mbs, Comp 10/17/12
5	BEAR LAKE COUNTY SD	33	MONTPELIER	5	1	325	155.00	18.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
6	BLACKFOOT SD	55	BLACKFOOT	6	2	1193	1000.00	100.00	A Complete	Fiber	Metro Ethemet (Agg)	CenturyLink	MOEUg -> 50 Mbps Acc Ord 3/18/13;
7	BLAINE COUNTY SD	61	CAREY	4	3	1111	1000.00	50.00	A Complete	Fiber	Metro Ethemet (Agg)	CenturyLink	
8	BLISS JOINT SD	234	BLISS	4	1	114	155.00	7.50	A Complete	Copper	5xT1-TDM (Agg)	CenturyLink	
9	BOISE CITY INDEPENDENT SD	1	BOISE	3	8	6203	1000.00	200.00	A Complete	Fiber	Metro Ethemet (Agg)	CenturyLink	
10	BONNEVILLE JOINT SD	93	IDAHO FALLS	6	3	3006	1000.00	100.00	A Complete	Fiber	Metro Ethemet (Agg)	CenturyLink	
11	BOUNDARY COUNTY SD	101	BONNERS FERRY	1	2	544	1000.00	30.00	A Complete	Fiber	DS3-TDM (Agg)	Frontier/Verizon	BW Inc from 21-30 Mbps Ord 03/28/13, Comp 04/26/13
12	BRUNEAU-GRAND VIEW JOINT SD	365	BRUNEAU	3	1	137	155.00	18.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	Fiber Upgd ord 05/10/13
13	BUHL JOINT SD	412	BUHL	4	1	375	155.00	12.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
14	BUTTE COUNTY JOINT SD	111	ARCO	6	1	143	1000.00	6.00	A Complete	Fiber	Syringa Ethernet (Agg)	Syringa/Albion	Syr Transition Ord 02/18/13, Comp 04/22/13
15	CALDWELL SD	132	CALDWELL	3	2	1628	1000.00	100.00	A Complete	Fiber	Metro Ethemet (Agg)	CenturyLink	BW Inc from 70-100 Ord 03/28/13
16	CAMAS COUNTY SD	121	FAIRFIELD	4	1	40	40.00	10.00	A Complete	Copper	Ethernet (Agg)	Syringa	Upgrade to 10 Mbps L2 Ord 05/16/13
17	CAMBRIDGE JOINT SD	432	CAMBRIDGE	3	1	83	1000.00	3.00	A Complete	Fiber	Syringa Ethernet (Agg)	Syringa/Cambridge	Syr Transition Ord 02/18/13, Comp 04/22/13
18	CASCADE SD	422	CASCADE	3	1	139	40.00	20.00	A Complete	Copper	Ethernet (Agg)	Syringa	Upgrade 20 Mbps L2 Ord 05/15/13
19	CASSIA COUNTY JOINT SD	151	BURLEY	4	6	1614	1000.00	100.00	A Complete	Fiber	Metro Ethemet (Agg)	CenturyLink	MOEUg -> 100 Mbps Acc Ord 3/19/13
20	CASTLEFORD SD	417	CASTLEFORD	4	1	268	155.00	21.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	BW Inc from 15-21 Ord 03/28/13, Comp 04/18/13
21	CHALLIS JOINT SD	181	CHALLIS	6	1	214	1000.00	20.00	A Complete	Fiber	Syringa Ethernet (Agg)	Syringa/Custer	Syr Transition Ord 02/18/13, Comp 04/22/13
22	CLARK COUNTY SD	161	DUBOIS	6	1	93	1000.00	10.00	A Complete	Fiber	Syringa Ethernet (Agg)	Syringa/Mud Lake	Syr Transition Ord 02/18/13, Comp 04/22/13
23	COEUR D'ALENE SDCharter	271	COEUR D'ALENE	1	1	626	1000.00	18.00	A Complete	Fiber	DS3-TDM (Agg)	Frontier/Verizon	
24	COEUR D'ALENE SDMain	271	COEUR D'ALENE	1	4	3091	1000.00	100.00	A Complete	Fiber	Ethernet->MPLS (Agg) Temp	Ednetics	
25	COMPASS CHARTER SCHOOL	455	MERIDIAN	3	1	510	1000.00	20.00	A Complete	Fiber	Metro Ethemet (Agg)	CenturyLink	
26	COSSA SD	555	0	3	1	107	300.00	20.00	FY2014	MW	MW Ethernet (Agg)	TecHut	New Connectin FY2014
27	COTTONWOOD JOINT SD	242	COTTONWOOD	2	1	205	155.00	15.00	A Complete	Copper	10xT1-TDM (Agg)	CenturyLink	
28	COUNCIL SD	13	COUNCIL	3	1	101	1000.00	6.00	A Complete	Fiber	Syringa Ethernet (Agg)	Syringa/Cambridge	Syr Transition Ord 02/18/13, Comp 04/22/13
29	CULDESAC JOINT SD	342	CULDESAC	2	1	90	155.00	7.50	A Complete	Copper	5xT1-TDM (Agg)	CenturyLink	BW Inc from 4.5-7.5 Comp 10/26/12
30	DIETRICH SD	314	DIETRICH	4	1	229	155.00	9.00	A Complete	Copper	6xT1-TDM (Agg)	CenturyLink	
31	EMMETT SD	221	EMMETT	3	3	584	1000.00	50.00	A Complete	Fiber	Metro Ethemet (Agg)	CenturyLink	Upg to 50Mbs MOE, Comp
32	FILER SD	413	FILER	4	1	409	1000.00	20.00	A Complete	Fiber	Syringa Ethernet (Agg)	Syringa/Filer Mutual Tel	Syr Transition Ord 02/18/13, Comp 04/22/13
33	FIRTH SD	59	FIRTH	6	1	219	155.00	21.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	BW Inc from 15.0 -> 21.0 Ord 01/14/13, Comp 02/19/13
34	FOREST BIRD CHARTER SD	84	SANDPOINT	1	1	267	100.00	30.00	FY2014	Copper	P-to-P LP Oreille WAN	Frontier/Verizon	New Connectin FY2014
35	FREMONT COUNTY JOINT SD	215	ST ANTHONY	6	3	815	1000.00	30.00	A Complete	Fiber	SyringaEthemet (Agg)	Syringa/Fairpoint	Syr Transition Ord 02/18/13, Comp 04/22/13
36	FRUITLAND SD	373	FRUITLAND	3	2	544	1000.00	50.00	A Complete	Fiber	SyringaEthemet (Agg)	Syringa/Farmers Mutual	Syr Transition Ord 02/18/13, Comp 04/22/13
37	GARDEN VALLEY SD	71	GARDEN VALLEY	3	1	115	40.00	10.00	A Complete	Copper	Ethernet (Agg)	Syringa	Upgrade to 10 Mbps L2 Ord 05/16/13
38	GENESEE JOINT SD	282	GENESEE	2	1	128	1000.00	15.00	A Complete	Fiber	DS3-TDM (Agg)	Frontier/Verizon	BW Inc from 12.0 -> 15.0 Mbs, Comp 02/11/13
39	GLENNS FERRY JOINT SD	192	GLENNS FERRY	4	1	148	155.00	6.00	A Complete	Copper	4xT1-TDM (Agg)	CenturyLink	
40	GOODING JOINT SD	231	GOODING	4	1	333	155.00	33.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	BW Inc from 24.0 -> 33.0 Ord 02/07/13 Comp 03/29/13
41	GRACE JOINT SD	148	GRACE	5	1	176	155.00	12.00	A Complete	Copper	8xT1-TDM (Agg)	CenturyLink	BW Inc from 7.5 -> 12.0 Mbs, Ord 02/07/13, Comp 3/20/13
42	HAGERMAN JOINT SD	233	HAGERMAN	4	2	216	155.00	21.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	BW Inc from 15.0 -> 21.0 Mbs, Ord 12/10/12, Comp 02/11/13
43	HANSEN SD	415	HANSEN	4	1	161	155.00	12.00	A Complete	Copper	8xT1-TDM (Agg)	CenturyLink	BW Inc from 9-12 Mbps Ord 03/28/13 comp 05/10/13
44	HIGHLAND JOINT SD	305	CRAIGMONT	0	1	159	155.00	9.00	A Complete	Copper	6xT1-TDM (Agg)	CenturyLink	BW Inc 6-9Mbs Ord 02/07/13 Comnp 03/25/13
45	HOMEDALE JOINT SD	370	HOMEDALE	3	2	372	1000.00	30.00	A Complete	Fiber	Ethernet (Agg)	Syringa	Upgrade 30 Mbps L2 Ord 05/16/13
46	HORSESHOE BEND SD	73	HORSESHOE BEND	3	1	97	40.00	20.00	A Complete	Copper	Ethernet (Agg)	Frontier/Citizens	Upgrade 20 Mbps L2 Ord 05/16/13

	School Data						Network Data						
	District	Dist No.	City	Reg	Num HS	HS Students Served	Architecture Capacity	Current IEN Purchased BW Per District (Mbs)	BW P & L Status	Current IEN Connection Media to District Aggregation Point	Current IEN Connectivity Circuit Type	Current IEN Connection Local Loop Provider	Comments
47	IDAHO ARTS CHARTER SCHOOL	788	NAMPA	3	1	605	1000.00	30.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	BW Inc from 30-40 Mbps Ord 03/26/13 Comp 05/06/13
48	IDAHO DISTANCE EDUCATION ACAD BOIS	288	BOISE	2	1	34	1000.00	30.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
49	IDAHO DISTANCE EDUCATION ACAD POCA	288	POCATELLO	2	1	21	100.00	10.00	A Complete	Copper	Metro Ethernet (Agg)	CenturyLink	
50	IDAHO DISTANCE EDUCATION ACAD POST	288	POST FALLS	2	1	65	24.00	4.50	A Complete	Copper	3XT1-TDM (Agg)	Frontier/Verizon	
51	IDAHO FALLS SD	91	IDAHO FALLS	6	4	3154	1000.00	100.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
52	IDAHO SCHOOL FOR THE DEAF & BLIND	960	GOODING	4	1	69	100.00	10.00	A Complete	Copper	Metro Ethernet (Agg)	CenturyLink	
53	iSUCCEED VIRTUAL HS	466	BOISE	3	1	754	100.00	5.00	A Complete	Copper	Metro Ethernet (Agg)	CenturyLink	
54	JEFFERSON COUNTY JOINT SD	251	MENAN	6	2	939	155.00	45.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
55	JEROME JOINT SD	261	JEROME	4	1	921	1000.00	100.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	MOE Ug -> 100 Mbps Acc 3/19/13
56	KAMIAH JOINT SD	304	KAMIAH	2	1	156	155.00	18.00	A Complete	Copper	12xT1-TDM (Agg)	CenturyLink	
57	KELLOGG JOINT SD	391	KELLOGG	1	2	432	1000.00	18.00	A Complete	Fiber	DS3-TDM (Agg)	Frontier/Verizon	
58	KENDRICK JOINT SD	283	KENDRICK	2	1	121	24.00	6.00	A Complete	Copper	4xT1-TDM (Agg)	Potlatch Telephone	
59	KIMBERLY SD	414	KIMBERLY	4	1	437	155.00	18.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
60	KOOTENAI BRIDGE ACADEMY	470	COEUR D'ALENE	1	1	201	24.00	7.50	A Complete	Copper	5xT1-TDM (Agg)	Frontier/Verizon	
61	KOOTENAI JOINT SD	274	HARRISON	1	1	131	24.00	6.00	A Complete	Copper	4xT1-TDM (Agg)	Frontier/Verizon	
62	KUNA JOINT SD	3	KUNA	3	2	1324	1000.00	100.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	BW Inc from 50 -> 100 Mbs Ord 02/19/13 Comp 3/26/13
63	LAKE PEND OREILLE SD	84	CLARK FORK	1	3	1252	1000.00	90.00	A Complete	Fiber	2xDS3-TDM (Agg)	Frontier/Verizon	
64	LAKELAND SD	272	RATHDRUM	1	4	1422	1000.00	54.00	A Complete	Fiber	2xDS3-TDM (Agg)	Frontier/Verizon	
65	LAPWAI SD	341	LAPWAI	2	1	262	155.00	9.00	A Complete	Copper	6xT1-TDM (Agg)	CenturyLink	
66	LEWISTON INDEPENDENT SD	340	LEWISTON	2	3	1122	155.00	45.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
67	LIBERTY CHARTER SCHOOL	458	NAMPA	3	1	396	1000.00	20.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
68	MACKAY JOINT SD	182	MACKAY	6	1	97	1000.00	5.00	A Complete	Fiber	Syringa Ethernet (Agg)	SyringaAlbion	Syr Transition Ord 02/18/13, Comp 04/22/13
69	MADISON SD	321	REXBURG	6	2	1033	1000.00	50.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	MOE Ug -> 50 Mbps Acc 3/19/13, Comp 05/15/13;
70	MARSH VALLEY JOINT SD	21	ARIMO	5	1	384	155.00	15.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
71	MARSING JOINT SD	363	MARSING	3	1	239	300.00	20.00	A Complete	MW	MW Ethernet (Agg)	TecHut	
72	MCCALL-DONNELLY SD	421	MC CALL	3	2	284	1000.00	30.00	A Complete	Fiber	Ethernet (Agg)	Syringa	Upgrade to 30 Mbps L2 Ord 05/16/13
73	MEADOWS VALLEY SD	11	NEW MEADOWS	3	1	172	40.00	10.00	A Complete	Copper	Ethernet (Agg)	Syringa	Upgrade 10 Mbps L2 Ord 05/16/13
74	MELBA JOINT SD	136	MELBA	3	2	357	155.00	18.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
75	MERIDIAN JOINT SD	2	MERIDIAN	3	10	9911	1000.00	300.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
76	MERIDIAN JOINT SD Charter 1	2	MERIDIAN	3	1	374	1000.00	30.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	BW Inc from 20.0 -> 30.0 Ord 02/07/13 Comp 03/26/13
77	MIDDLETON SD	134	MIDDLETON	3	2	987	1000.00	200.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	BW Inc from 40 -> 200 Ord 04/29/13 Comp 05/24/13
78	MIDVALE SD	433	MIDVALE	3	2	86	1000.00	9.00	A Complete	Fiber	Syringa Ethernet (Agg)	Syringa/Midvale Tel	Syr Transition Ord 02/18/13, Comp 04/22/13
79	MINIDOKA COUNTY JOINT SD	331	HEYBURN	4	1	161	155.00	6.00	A Complete	Copper	4xT1-TDM (Agg)	CenturyLink	
80	MINIDOKA COUNTY JOINT SD Main	331	RUPERT	4	2	1265	1000.00	50.00	A Complete	Fiber	Syringa Ethernet (Agg)	Syringa/PMT	Syr Transition Ord 02/18/13, Comp 04/22/13
81	MOSCOW SD	281	MOSCOW	2	2	571	1000.00	24.00	A Complete	Fiber	DS3-TDM (Agg)	Frontier/Verizon	
82	MOUNTAIN HOME SD	193	MOUNTAIN HOME	3	1	1023	1000.00	50.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
83	MOUNTAIN VIEW SD	244	KOOSKIA	2	2	461	155.00	18.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
84	MULLAN SD	392	MULLAN	1	1	55	1000.00	9.00	A Complete	Copper	4xT1-TDM (Agg)	Frontier/Verizon	
85	MURTAUGH JOINT SD	418	MURTAUGH	4	1	47	155.00	3.00	A Complete	Copper	2xT1-TDM (Agg)	CenturyLink	
86	NAMPA SD	131	NAMPA	3	6	4040	1000.00	200.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
87	NEW PLYMOUTH SD	372	NEW PLYMOUTH	3	1	288	155.00	18.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
88	NEZPERCE JOINT SD	302	NEZPERCE	2	1	78	155.00	9.00	A Complete	Copper	4xT1-TDM (Agg)	CenturyLink	

	School Data						Network Data						
	District	Dist No.	City	Reg	Num HS	HS Students Served	Architecture Capacity	Current IEN Purchased BW Per District (Mbs)	BW P & L Status	Current IEN Connection Media to District Aggregation Point	Current IEN Connectivity Circuit Type	Current IEN Connection Local Loop Provider	Comments
89	NORTH GEM SD	149	BANCROFT	5	1	89	155.00	7.50	A Complete	Copper	5xT1-TDM (Agg)	CenturyLink	
90	NORTH STAR CHARTER SCHOOL	2	EAGLE	3	1	914	1000.00	20.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
91	NORTH VALLEY ACADEMY	465	GOODING	4	1	209	100.00	10.00	A Complete	Copper	Metro Ethernet (Agg)	CenturyLink	
92	NOTUS SD	135	NOTUS	3	1	162	1000.00	20.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
93	ONEIDA COUNTY SD	351	MALAD CITY	5	2	272	1000.00	20.00	A Complete	Fiber	SyringaEthernet (Agg)	Syringa/Albion	Syr Transition Ord 02/18/13, Comp 04/22/13
94	OROFINO JOINT SD	171	OROFINO	2	2	468	1000.00	21.00	A Complete	Fiber	DS3-TDM (Agg)	Frontier/Verizon	
95	PARMA SD	137	PARMA	3	1	328	300.00	20.00	A Complete	MW	MW Ethernet (Agg)	TecHut	
96	PAYETTE JOINT SD	371	PAYETTE	3	2	512	1000.00	50.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	MOE Ug -> 50 Mbps Acc Ord 3/19/13
97	PLUMMER/WORLEY JOINT SD	44	PLUMMER	1	1	128	24.00	6.00	A Complete	Copper	4xT1-TDM (Agg)	Frontier/Verizon	
98	POCATELLO SD	25	POCATELLO	5	5	3700	1000.00	200.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	BW Inc from 100.0 -> 200.0 Mbs, Ord 02/07/13 Comp 03/25/13
99	POST FALLS SD	273	POST FALLS	1	2	1606	1000.00	65.00	A Complete	Fiber	OC3-TDM (Agg)	Frontier/Verizon	
100	POTLATCH SD	285	POTLATCH	2	1	181	155.00	9.00	A Complete	Fiber	DS3-TDM (Agg)	Frontier/Verizon	
101	PRESTON JOINT SD	201	PRESTON	5	2	711	155.00	27.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
102	RICHARD McKENNA CHARTER HIGH	ID	MOUNTAIN HOME	3	1	136	1000.00	50.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
103	RICHFIELD SD	316	RICHFIELD	4	1	187	155.00	7.50	A Complete	Copper	5xT1-TDM (Agg)	CenturyLink	
104	RIRIE JOINT SD	252	RIRIE	6	1	209	155.00	9.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
105	ROCKLAND SD	382	ROCKLAND	5	1	145	1000.00	10.00	A Complete	Fiber	Syringa Ethernet (Agg)	Syringa/Direct Comm	Syr Transition Ord 02/18/13, Comp 04/22/13
106	SALMON RIVER JOINT SD	243	RIGGINS	2	1	59	40.00	10.00	A Complete	Copper	Ethernet (Agg)	Syringa	
107	SALMON SD	291	SALMON	6	2	314	1000.00	25.00	A Complete	Fiber	Ethernet (Agg)	Custer Telephone	BW Upg from 15 -> 25 Mbps Layer2 Ord 3/28/13 Comp 04/1/13
108	SHELLEY JOINT SD	60	SHELLEY	6	1	629	1000.00	50.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	MOE Ug -> 50 Mbps Acc 3/18/13, Comp 05/16/13;
109	SHOSHONE JOINT SD	312	SHOSHONE	4	2	166	155.00	15.00	A Complete	Copper	10xT1-TDM (Agg)	CenturyLink	
110	SNAKE RIVER SD	52	BLACKFOOT	5	1	531	1000.00	50.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	MOE Ug -> 50 Mbps Acc 3/18/13 Comp 05/15/13
111	SODA SPRINGS JOINT SD	150	SODA SPRINGS	5	1	244	155.00	9.00	A Complete	Copper/Fiber	6xT1-TDM	CenturyLink	
112	SOUTH LEMHI SD	292	LEADORE	6	1	69	155.00	6.00	A Complete	Copper	4xT1-TDM (Agg)	CenturyLink	
113	ST MARIES JOINT SD	41	ST MARIES	1	2	348	155.00	18.00	A Complete	MW	MW-DS3-TDM (Agg)	First Step Lewiston	
114	STATE JUVENILE CORRECTION DISTRICT -	709	LEWISTON	4	1	36	24.00	3.00	A Complete	Copper	2xT1-TDM (Agg)	CenturyLink	
115	STATE JUVENILE CORRECTION DISTRICT -	709	NAMPA	4	1	84	100.00	10.00	A Complete	Copper	Metro Ethernet (Agg)	CenturyLink	
116	STATE JUVENILE CORRECTION DISTRICT -	709	ST ANTHONY	4	1	120	24.00	4.50	A Complete	Copper	3xT1-TDM (Agg)	Fairpoint	
117	SUGAR-SALEM JOINT SD	322	SUGAR CITY	6	2	445	155.00	33.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
118	TAYLORS CROSSING CHARTER SCHOO	461	IDAHO FALLS	6	1	381	1000.00	20.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
119	TETON COUNTY SD	401	DRIGGS	6	1	414	1000.00	30.00	A Complete	Fiber	Syringa Ethernet (Agg)	Syringa/Columbine Telco Silver Star	Syr Transition Ord 02/18/13, Comp 04/22/13
120	TROY SD	287	TROY	2	1	169	24.00	7.50	A Complete	Copper	4xT1-TDM (Agg)	Potlatch Telephone	
121	TWIN FALLS SD	411	TWIN FALLS	4	3	2275	1000.00	250.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
122	VALLIVUE SD	139	CALDWELL	3	3	2108	1000.00	100.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
123	VICTORY CHARTER SCHOOL	451	Nampa	3	1	380	1000.00	20.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
124	VISION CHARTER SCHOOL	463	CALDWELL	3	1	436	1000.00	30.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
125	WALLACE SD	393	WALLACE	1	1	235	1000.00	18.00	A Complete	Copper	12xT1-TDM	Frontier/Citizens	
126	WEISER SD	431	WEISER	3	2	533	1000.00	50.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	MOE Ug -> 50 Mbps Acc Ord 3/18/13 Comp 05/30/13
127	WENDELL SD	232	WENDELL	4	1	304	155.00	15.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink	
128	WEST BONNER COUNTY SD	83	PRIEST RIVER	1	2	448	1000.00	30.00	A Complete	Fiber	DS3-TDM (Agg)	Frontier/Verizon	
129	WEST JEFFERSON SD	253	TERRETON	6	1	164	1000.00	20.00	A Complete	Fiber	SyringaEthernet (Agg)	Syringa/Mud Lake Telephone Coop	Syr Transition Ord 02/18/13, Comp 04/22/13
130	WEST SIDE SD	202	DAYTON	5	1	179	155.00	12.00	A Complete	Copper	8xT1-TDM (Agg)	CenturyLink	
131	WHITEPINE JOINT SD	288	DEARY	2	1	189	24.00	7.50	A Complete	Copper	5xT1-TDM (Agg)	Frontier/Verizon	
132	WILDER SD	133	WILDER	3	1	191	300.00	20.00	A Complete	MW	MW Ethernet (Agg)	TecHUT	
133	XAVIER CHARTER SCHOOL	462	TWIN FALLS	4	1	574	1000.00	20.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
134	Y College of Southern Idaho	N/A	TWIN FALLS	4	0	0	1000.00	20.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
135	Y College of Western Idaho	N/A	Nampa	3	0	0	1000.00	20.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
136	Y Eastern Idaho Technical College	N/A	IDAHO FALLS	6	0	0	1000.00	20.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
137	Y Idaho Digital Learning Academy	N/A	BOISE	3	0	0	1000.00	20.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink	
138	Y2 Boise State University	N/A	BOISE	5	0	0	24.00	0.00	HE Complete	Fiber	IRON Ethernet (Agg)	IRON	
139	Y2 Idaho State University	N/A	POCATELLO	6	0	0	24.00	0.00	HE Complete	Fiber	IRON Ethernet (Agg)	IRON	
140	Y2 Lewis and Clark State College	N/A	LEWISTON	8	0	0	24.00	0.00	HE Complete	Fiber	IRON Ethernet (Agg)	IRON	
141	Y2 North Idaho College	N/A	COEUR D'ALENE	7	0	0	24.00	0.00	HE Complete	Fiber	IRON Ethernet (Agg)	IRON	
142	Y2 University of Idaho	N/A	MOSCOW	4	0	0	24.00	0.00	HE Complete	Fiber	IRON Ethernet (Agg)	IRON	
143	Z First Step - Lewiston	N/A	LEWISTON	0	0	0	155.00	18.00	A Complete	Fiber	DS3-TDM (Agg)	CenturyLink -> First Step Lewiston	
144	Z TecHUT Boise	N/A	BOISE	0	0	0	1000.00	100.00	A Complete	Fiber	Metro Ethernet (Agg)	CenturyLink -> TecHut Boise	
					217	85,642	81,731.00	4,921.50					

COMMUNICATIONS REPORT

The Idaho Education Network continues to offer solutions by providing access, collaboration and opportunity for students and communities across the state. **Access** for students to take hard to find and dual credit courses; **collaborations** for school boards, administrators and teachers to explore innovative practices in curriculum and technology, and **opportunities** for communities to build on their educational programs for students, parents or community members. The quality broadband network supports all districts and their individual needs while the video conferencing capabilities are limited only by imagination.

➢ Access

The 2013-2014 IEN Course Catalog has been mailed to each school that has an IEN video teleconference system. It features wonderful courses such as the History of Rock which is a dual credit course from Ms. McMullin in Genesee. The catalog is updated each month and posted on our website. The catalog does not include the school consortiums that share courses - the consortiums include Meridian School District, Bonneville School District, the Upper Snake River and Bear Lake Consortiums, as well as several others. An interactive map of IEN school locations and consortiums can be found on the website at www.ien.idaho.gov/resources/ien_map_consortium.html.

The May 2013 issue of ISBA Slate Magazine features a student from Weiser High School – Nathan Eliason. The article was written by the IEN's PR and Communications Specialist, Kristin Magruder, and was subsequently picked up by Idaho Education News. Nathan discusses the opportunities afforded to him via the Idaho Education Network gaining access to great teachers like Jason Torgrimson of Twin Falls. Jason continues to offer his wonderful courses (see the 2013-2014 IEN Course Catalog) and Nathan plans to take Calculus II next year from Dave Gural at IDLA via their IEN system.

➢ Collaborations

The IEN continues to live up to the title of 'Network,' working with organizations inside and outside Idaho to increase opportunities for both educators and students. The IEN staff has been busy participating in national conferences including a distance education conference in St. Louis last May. Brady Kraft will be presenting at ISTE in June and the IEN will have two sessions at the Idaho Association of School Administrators conference in July.

Brady Kraft continues to participate actively in the Internet2 K20 Advisory Council (www.internet2.edu/k20/) and Julie Best is chairing the Distance Learning SIG for the Visual Communications Industry Group (www.vci-group.org).

We have been working with schools, companies, and other agencies to support the Albertsons Foundation's PTECH grant initiative.

The Idaho Education Network was honored and featured by the National Journal on Innovation. Director Teresa Luna has been asked to participate in a policy panel discussion in Washington, D.C. on the Idaho Education Network and we will be featured in their special June Innovation Edition.

➢ Opportunities

Fifteen elementary schools around the state of Idaho have been awarded an interactive video conference system that has been designed to meet the needs of the elementary environment. The goal of the pilot project is to gather data and feedback from the participants in hopes of expanding the IEN into all grade levels. The following schools were awarded systems:

- Barbara Morgan STEM Academy, Meridian
- Donnelly Elementary School, Donnelly
- Galileo STEM Academy, Meridian
- Hayden Meadows Elementary School, Coeur d'Alene
- Homedale Elementary School, Homedale
- Idaho Distance Education Academy, Boise
- North Idaho STEM Charter Academy, Rathdrum
- Ponderosa Elementary School, Post Falls
- Ramsey Magnet School of Science, Coeur d'Alene
- Rulon Ellis Elementary School, Chubbuck
- Sacajawea Elementary School, Caldwell
- Snake River Middle School, Blackfoot
- Star Elementary School, Star
- Summerwind School of Math and Science, Boise
- Shadow Butte Elementary, Emmett

The IEN has been working with the Library of Congress to establish a relationship with the Colleges of Education to offer pre-service workshops via the IEN on primary source research.

➢ Website Social Media Outreach

The IEN website (www.ien.idaho.gov) recently went live with an updated look and feel. The content was reorganized for clarity and the site was given IEN branding. New website additions include interactive forms for scheduling events, reporting technical support issues, and requesting training. Visitors can

now use an updated interactive map to quickly find IEN locations and contact information and resources have been categorized to help visitors find information quickly. Other features include a more robust media section, a live Twitter feed, and media toolkit.

The IEN continues to use Twitter as the primary social media tool to connect with Ed Tech networks and the public. Currently at 246 followers, the focus is on IEN activities and distance learning opportunities. IEN recently sponsored a virtual field trip for Idaho Arts Charter School, where 1st and 2nd graders visited the Alaska SeaLife Center to learn about avian habitat. Their trip was concluded by making the tufted puffins pictured at left.

This page intentionally left blank

IDAHO EDUCATION NETWORK

TECHNOLOGY
Brady Kraft Director
(208) 332-1840

Mike Costa VTC Program Specialist
(208) 332-1839

Michael Bartz Administrative Assistant
(208) 332-1801

COMMUNICATIONS
Julie Best Director
(208) 332-1832

Kristin Magruder PR & Communications Specialist
(208) 332-1842

650 West State Street Room 100
P.O. Box 83720, Boise ID 83720-0304
www.ien.idaho.gov
